

ABBVIE

Edge Delivery Services Migration

Milestone 1: Discovery & Planning Deliverables

AEM to Edge Delivery Services Transformation

Prepared by: Adobe Consulting Services
Document Version: 1.0 | February 2026
Classification: Adobe/AbbVie Confidential

Table of Contents

- 1. AbbVie Boilerplate Requirements
- 2. Sites Priority & Sequencing
- 3. Technical Team Onboarding & Access Setup
- 4. Project Kickoff Materials
- 5. Draft Migration Schedule
- 6. Milestone Review Criteria
- 7. Content Operations Assessment

1. AbbVie Boilerplate Requirements

1.1 Boilerplate Configuration

Requirement	Specification	Priority
Repository Structure	Standard EDS boilerplate with AbbVie customizations	P0
Design Token System	CSS custom properties for brand colors, typography, spacing	P0
Header/Footer Templates	Global experience fragments migrated to EDS blocks	P0
ISI Component	Pharmaceutical-compliant Important Safety Information block	P0
Cookie Consent	OneTrust integration for GDPR/CCPA compliance	P0
Analytics Integration	Adobe Launch + Adobe Analytics tracking	P1
Search Integration	Site search capability (Adobe Search or alternative)	P1
Language/Locale Support	Multi-language content structure (30+ locales)	P1

1.2 Performance Targets

95+

Lighthouse Score

<2.5s

LCP Target

<100ms

FID Target

<0.1


CLS Target

1.3 Core Block Library

Block	Variants	Priority
header	standard, minimal, mega-menu	P0
footer	standard, multi-column	P0
hero	full-width, split, video-bg	P0
cards	2-col, 3-col, 4-col, featured	P0
accordion	standard, faq-style	P0
isi	sticky, inline, modal	P0
carousel	hero, testimonial, product	P1

2. Sites Priority & Sequencing

2.1 AbbVie Digital Ecosystem

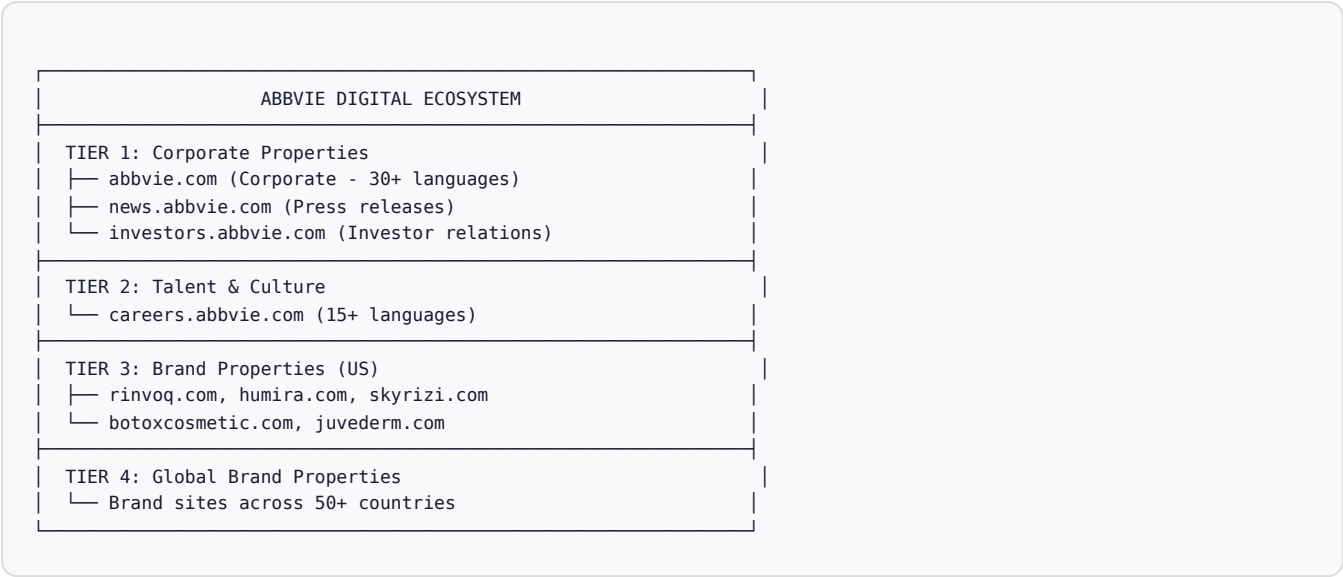

2.2 Recommended Migration Sequence

Phase	Site(s)	Pages	Duration	Rationale
Pilot	news.abbvie.com	100 templates	8 weeks	Lower risk, proves automation
Phase 1	abbvie.com (EN)	350-450	24 weeks	Corporate flagship
Phase 2	careers.abbvie.com	100/lang	12 weeks	Leverages Phase 1 components
Phase 3	investors.abbvie.com	50-80	8 weeks	Specialized IR requirements
Phase 4	abbvie.com (Global)	3,000+	36 weeks	Localization at scale
Phase 5	Brand sites (Priority)	1,000+	24 weeks	RINVOQ, Skyrizi, Humira

2.3 Site Priority Matrix

Site	Business Impact	Technical Complexity	Risk	Priority
abbvie.com (EN)	High	Medium	Medium	P1
news.abbvie.com	Medium	Low	Low	P0 (Pilot)
careers.abbvie.com	Medium	Medium	Low	P2
investors.abbvie.com	High	Low	Low	P2
rinvoq.com	High	High	High	P3

3. Technical Team Onboarding & Access Setup

3.1 Access Requirements

Role	GitHub Access	Repository
Adobe Architects	Admin	abbvie-eds/*
Adobe Developers	Write	abbvie-eds/*
AbbVie Tech Leads	Admin	abbvie-eds/*
AbbVie Developers	Write	abbvie-eds/*
AbbVie Content Authors	Read	abbvie-eds/content-*

3.2 Onboarding Checklist


Week 1: Environment Setup

- ☐ GitHub organization created
- ☐ Team members added with roles
- ☐ SSH keys configured
- ☐ Local dev environment verified
- ☐ AEM CLI installed

Week 2: Training

- ☐ EDS Architecture overview (4 hrs)
- ☐ Block development workshop (8 hrs)
- ☐ Content authoring training (4 hrs)
- ☐ CI/CD pipeline walkthrough (2 hrs)
- ☐ Preview/Publish workflow (2 hrs)

3.3 Team Structure

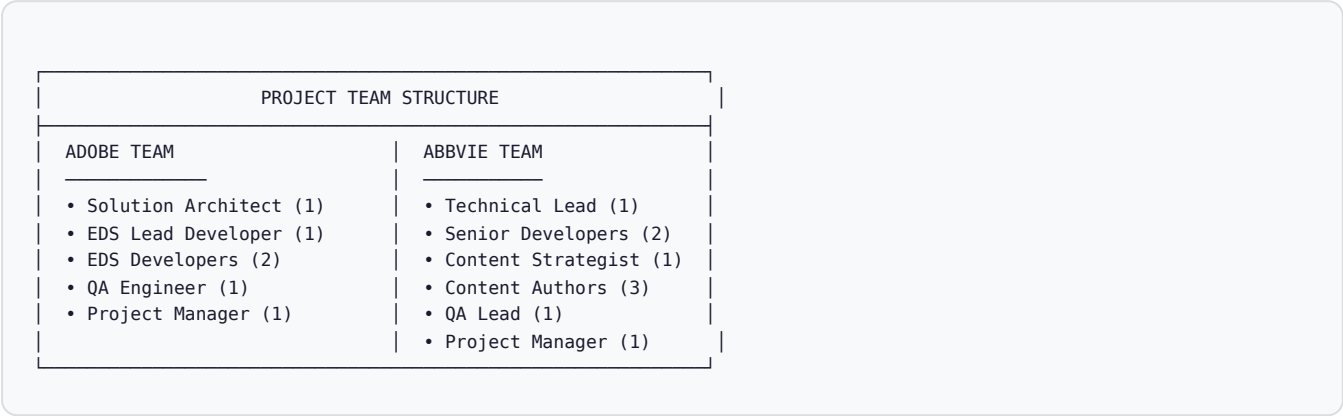

4. Project Kickoff Materials

4.1 Project Objectives

Objective	Success Criteria	Measurement
Performance	Lighthouse 95+ on all pages	Automated testing
Cost Reduction	65-80% infrastructure savings	Annual TCO comparison
Content Velocity	10x faster publish times	Time-to-publish metrics
Author Experience	80%+ author satisfaction	Survey results
Compliance	Zero MLR violations	Audit results

4.2 Communication Plan


Channel	Purpose	Frequency
Slack (#abbvie-eds)	Daily collaboration	Real-time
Weekly Status	Progress review	Weekly (Tuesdays)
Steering Committee	Executive updates	Bi-weekly
Sprint Reviews	Demo completed work	Every 2 weeks

4.3 Risk Register

Risk	Probability	Impact	Mitigation
MLR review delays	High	High	Parallel review tracks, early submission
Resource availability	Medium	High	Cross-training, documentation
Scope creep	Medium	Medium	Change control process
Integration complexity	Medium	High	Early POCs, architecture review

5. Draft Migration Schedule

5.1 High-Level Timeline

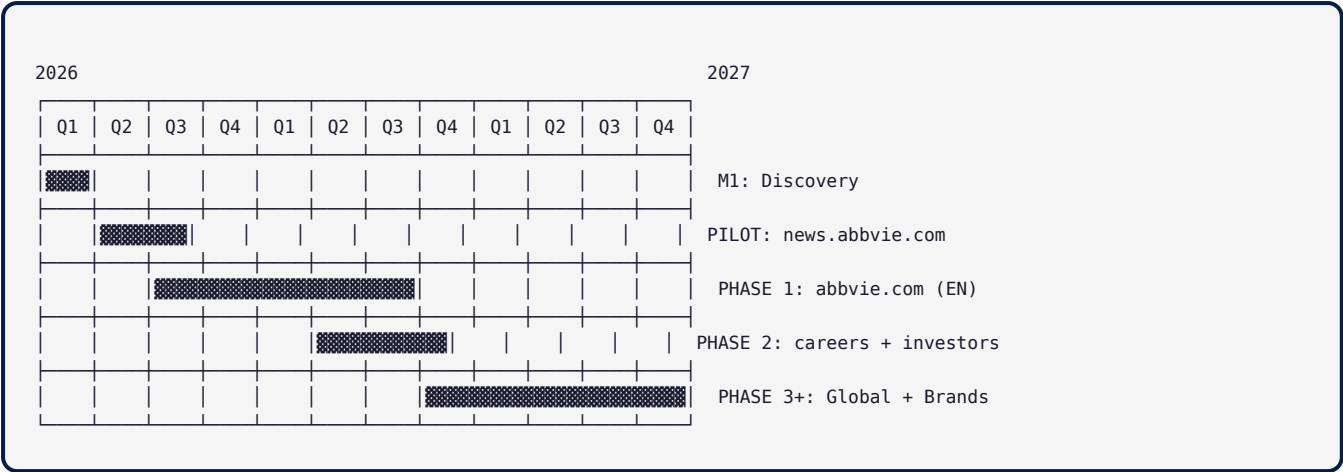

5.2 Milestone Schedule

Milestone	Target	Deliverables
M1: Discovery	Week 4	Requirements, sequencing, kickoff materials
M2: Pilot Launch	Week 16	news.abbvie.com live on EDS
M3: Phase 1 Start	Week 18	abbvie.com migration begins
M4: Block Library	Week 30	Core blocks complete
M5: Content 50%	Week 38	50% of EN content migrated
M6: Phase 1 Launch	Week 48	abbvie.com (EN) live

6. Milestone Review Criteria

6.1 Milestone 1 Exit Criteria

Deliverable	Acceptance Criteria	Status
Requirements Document	Signed off by AbbVie Tech Lead	☐
Site Sequencing	Approved by Steering Committee	☐
Team Onboarding	All team members with access	☐
Kickoff Materials	Distributed to all stakeholders	☐
Migration Schedule	Baselined and approved	☐
Content Ops Assessment	Findings reviewed with AbbVie	☐

6.2 Quality Gates


Gate	Criteria	Responsible
Architecture Review	Solution design approved	Solution Architect
Security Review	No critical vulnerabilities	Security Team
Accessibility Audit	WCAG 2.1 AA compliant	QA Lead
Performance Validation	Lighthouse 95+	Tech Lead
MLR Approval	All pharma content approved	AbbVie MLR Team

7. Content Operations Assessment

7.1 Current Pain Points

Pain Point	Impact	EDS Solution
Slow publish times (2-4 hours)	Missed opportunities	<30 min publish
Complex authoring UI	Author frustration	Document-based authoring
Heavy approval workflows	Bottlenecks	Streamlined preview/publish
Inconsistent experiences	Brand dilution	Shared block library
High infrastructure costs	Budget strain	CDN-only architecture

7.2 Recommended Governance Model

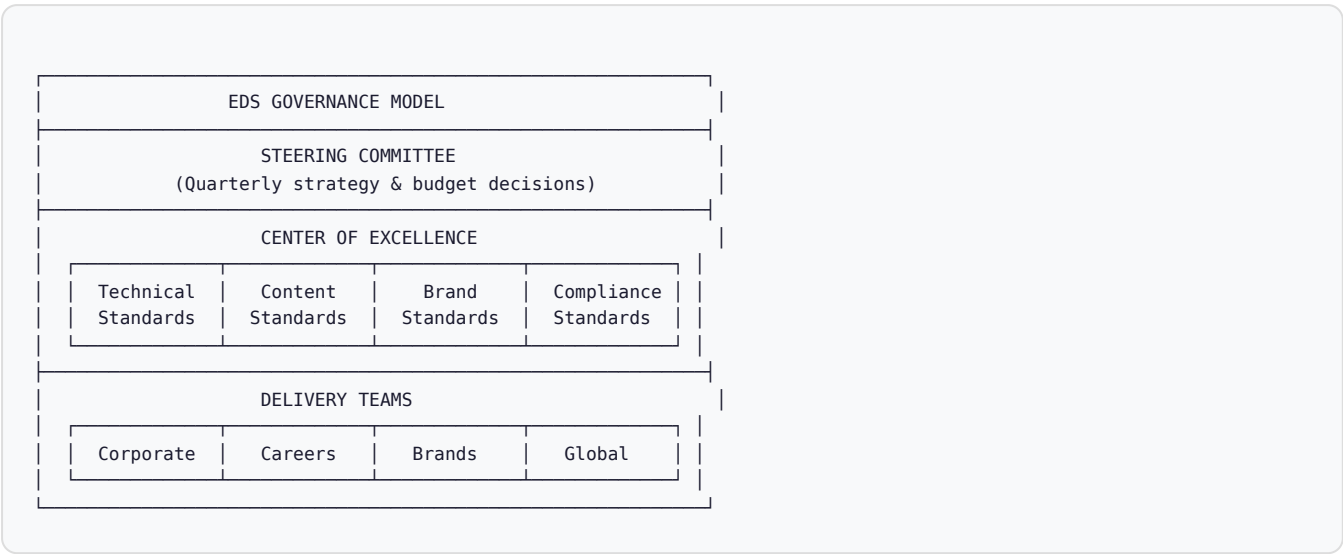

7.3 Training Requirements

Audience	Training	Duration	Priority
Content Authors	Document authoring, preview workflow	4 hours	P0
Developers	EDS block development, CI/CD	16 hours	P0
Tech Leads	EDS architecture, best practices	8 hours	P0
QA Team	EDS testing, Lighthouse, accessibility	8 hours	P1
Stakeholders	EDS overview, benefits, expectations	2 hours	P1

Document Approval

Role	Name	Signature	Date
Adobe Solution Architect			
Adobe Project Manager			
AbbVie Technical Lead			
AbbVie Project Manager			
AbbVie Executive Sponsor			

Document Version: 1.0 | **Date:** February 2026
Classification: Adobe/AbbVie Confidential
Next Review: Milestone 1 Review Session
